CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

COMMERCIAL HVAC / CONDITION REPORT

Arrigo CDJR Sawgrass

Required replacements & water damage

5901 Madison Avenue | Tamarac, FL 33321



PRIORITY ACTIONS

Immediate service: Unit 1 flooding.

Required replacements: Units 3, 7, 9 and 10.

Roof water damage: evaluate ponding, staining and wet areas.

Recommended combined work: replace Unit 8 with Unit 7.

Inspection: September 29, 2026 | Updated: October 9, 2026

Prepared by O'Brien AC & Construction Services, LLC
(954) 205-1381

Building photo: CarGurus / Arrigo Sawgrass listing

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

01 / REPLACEMENT PRIORITIES

Required replacement summary

REPLACEMENT REQUIRED - UNITS 3, 7, 9 AND 10

UNIT	LOCATION / CONDITION	ACTION
3	Non-functional; shut off. Significant wear documented.	Replace
7	Finance Department	Replace
9	Second Floor - Executive and Executive Assistant	Replace
10	Service Advisor Area	Replace

UNIT 1 | IMMEDIATE SERVICE

Water is releasing from multiple areas of the unit body. Immediate service is required to locate the source, stop active discharge and address the flooding condition.

UNIT 8 | RECOMMENDED WITH UNIT 7


Unit 8 serves the Showroom Mezzanine and is near the end of its service life. We recommend replacing it with Unit 7 to reduce repeat work in the same area.

Photo locations in this report follow the supplied folder labels. No new Unit 3 photo folder was provided; its replacement requirement is retained from the condition findings and updated service direction.

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

02 / SITE OVERVIEW

Rooftop unit locations & status

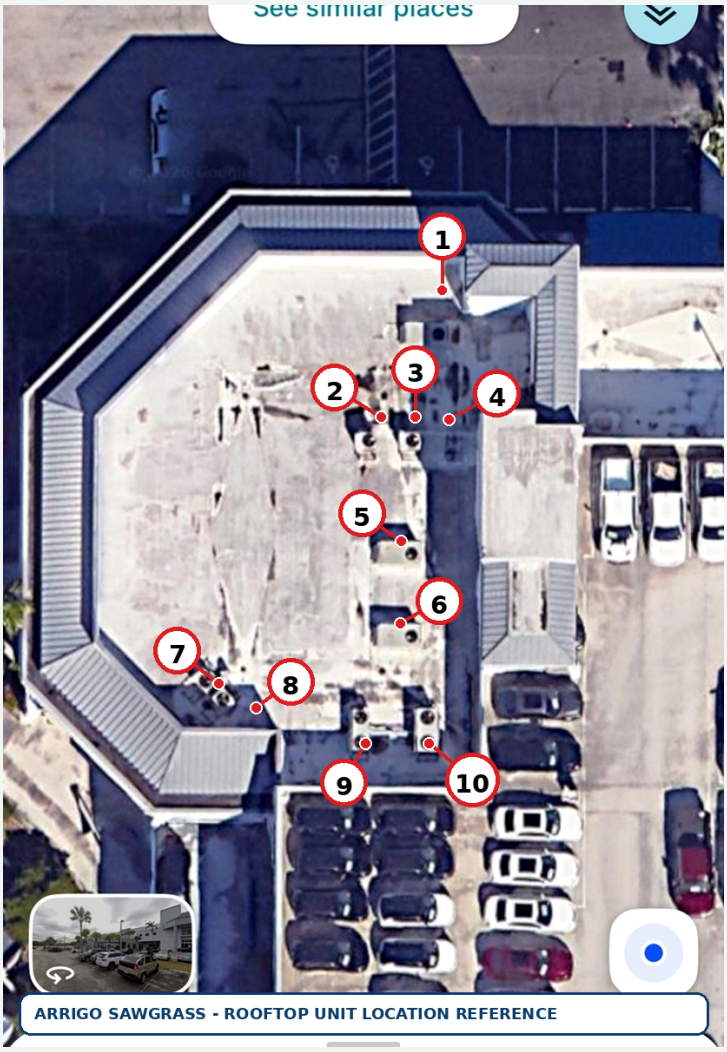

CURRENT STATUS

UNIT 01
Immediate service - flooding

UNIT 02
Repaired - monitor

UNIT 03
Replacement required

UNIT 04
Maintenance / repair review

UNIT 05
Operational - maintain

UNIT 06
Operational - maintain

UNIT 07
Replace - Finance

UNIT 08
Recommend with Unit 7

UNIT 09
Replace - Executive area

UNIT 10
Replace - Service Advisor

HOW TO READ THE LOCATION MAP

Numbered markers identify unit locations from the supplied rooftop reference. Marker outlines are location identifiers; the adjacent status list shows the current service and replacement priorities.

Critical / replacement: Units 1, 3, 7, 9 and 10.
Service / monitor / planned replacement: Units 2, 4 and 8.
Operational / maintain: Units 5 and 6.

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

03 / ALL TEN UNITS

Unit-by-unit condition matrix

UNIT	CURRENT FINDING	RECOMMENDED ACTION
1	Flooding; water releasing from multiple areas of the unit body.	IMMEDIATE SERVICE Locate and stop water release.
2	Repaired; adequate operation achieved.	Monitor operation; maintain.
3	Shut off / non-functional; significant wear.	REPLACEMENT REQUIRED
4	Maintenance needed; possible improper prior repairs.	Maintain and review prior repairs.
5	Operational.	Continue preventive maintenance.
6	Operational.	Continue preventive maintenance.
7	Finance Department; abnormal operation and loud noise previously documented.	REPLACEMENT REQUIRED Coordinate work with Unit 8.
8	Showroom Mezzanine; near end of service life.	Recommend replacement with Unit 7.
9	Second Floor - Executive and Executive Assistant; non-functional.	REPLACEMENT REQUIRED
10	Service Advisor Area; non-functional.	REPLACEMENT REQUIRED

Unit 8 is a recommended combined replacement; the required replacement group remains Units 3, 7, 9 and 10.

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

04 / ROOF AND FLOODING CONDITIONS

Water damage & immediate service

UNIT 1 - IMMEDIATE ATTENTION FOR SERVICE

Unit 1 is flooding, with water coming from multiple areas of the unit body. Stop the active water release and assess affected roof, electrical and interior areas.



Standing water and wet roof areas around rooftop equipment.



Surface staining and ponding near equipment and piping.

REQUIRED CORRECTIVE WORK

Service Unit 1 immediately. Evaluate condensate discharge, roof drainage, membrane condition and local slope together. Coordinate HVAC corrections with roof and drainage repairs to limit continued water exposure.

The photographs document ponding, wet areas and staining; they do not establish one cause or the full extent of roof damage.

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

05 / UNIT DOCUMENTATION

Unit 7 | Finance Department

REPLACEMENT REQUIRED



Unit 7 | IMG_4039



Unit 7 | IMG_4041



Unit 7 | IMG_4040

Location label: unit 7 Finance department

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026


05 / UNIT DOCUMENTATION

Unit 9 | Second Floor - Executive & Executive Assistant

REPLACEMENT REQUIRED



Unit 9 | IMG_4048

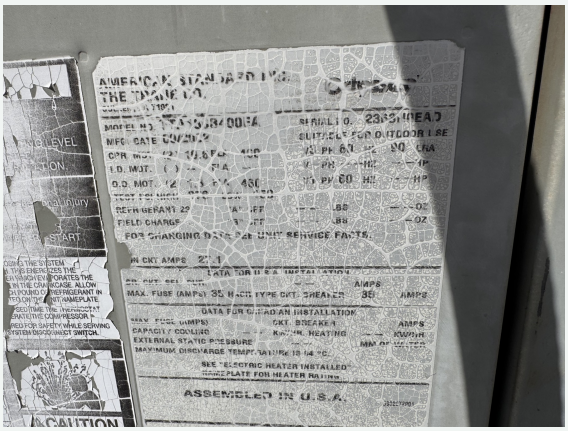

Unit 9 | IMG_4047



Unit 9 | IMG_4046

Location label: unit 9 second floor executive and excutive assistant

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

05 / UNIT DOCUMENTATION

Unit 10 | Service Advisor Area

REPLACEMENT REQUIRED



Unit 10 | IMG_4049



Unit 10 | IMG_4052



Unit 10 | IMG_4051



Unit 10 | IMG_4050

Location label: unit 10 service advisor area

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

06 / COMBINED REPLACEMENT RECOMMENDATION

Unit 8 | Showroom Mezzanine

RECOMMENDED REPLACEMENT WITH UNIT 7



Unit 8 | IMG_4045



Unit 8 | IMG_4044



Unit 8 | IMG_4043



Unit 8 | IMG_4042

REPLACE UNITS 7 AND 8 TOGETHER

Unit 7 requires replacement and Unit 8 is near the end of its service life. Completing both in the same work area can provide substantial savings by avoiding repeat mobilization, access, setup and labor within a short period.

Combined pricing and savings will be confirmed in the replacement proposal.

CUSTOMER	PROPERTY	REPORT UPDATE
Arrigo CDJR Sawgrass	5901 Madison Ave, Tamarac, FL 33321	October 9, 2026

07 / APPROVAL AND COORDINATION

Recommended corrective action plan

CRITICAL

Unit 1 | Immediate service

Locate and stop active water release. Document the source and assess affected areas.

REQUIRED

Units 3, 7, 9 and 10 | Replacement

Approve replacement scopes. Verify capacity, electrical service, supports, piping and access before selecting equipment.

URGENT

Roof | Water damage

Coordinate condensate corrections with roof drainage and membrane evaluation. Confirm the affected areas and roof repair scope.

RECOMMENDED

Unit 8 | Combine with Unit 7

Replace both together to reduce repeat work in the Finance / Showroom Mezzanine area. Confirm combined savings in the proposal.

SERVICE / MONITOR

Units 2 and 4 | Follow-up

Monitor Unit 2 after repair. Maintain Unit 4 and review possible improper prior repairs.

ROUTINE

Units 5 and 6 | Preventive maintenance

Schedule two visits per year for viable equipment. Inspect coils, pans and condensate drainage; keep discharge paths clear.

AFTER COMPLETION

Verify operation and drainage after corrective work. Document completed work and any remaining roof repairs.

Service and replacement approvals | (954) 205-1381
